


Calvert Area Liaison Meeting

16th December 2021

David Griffiths-Allen
Richard Maxwell

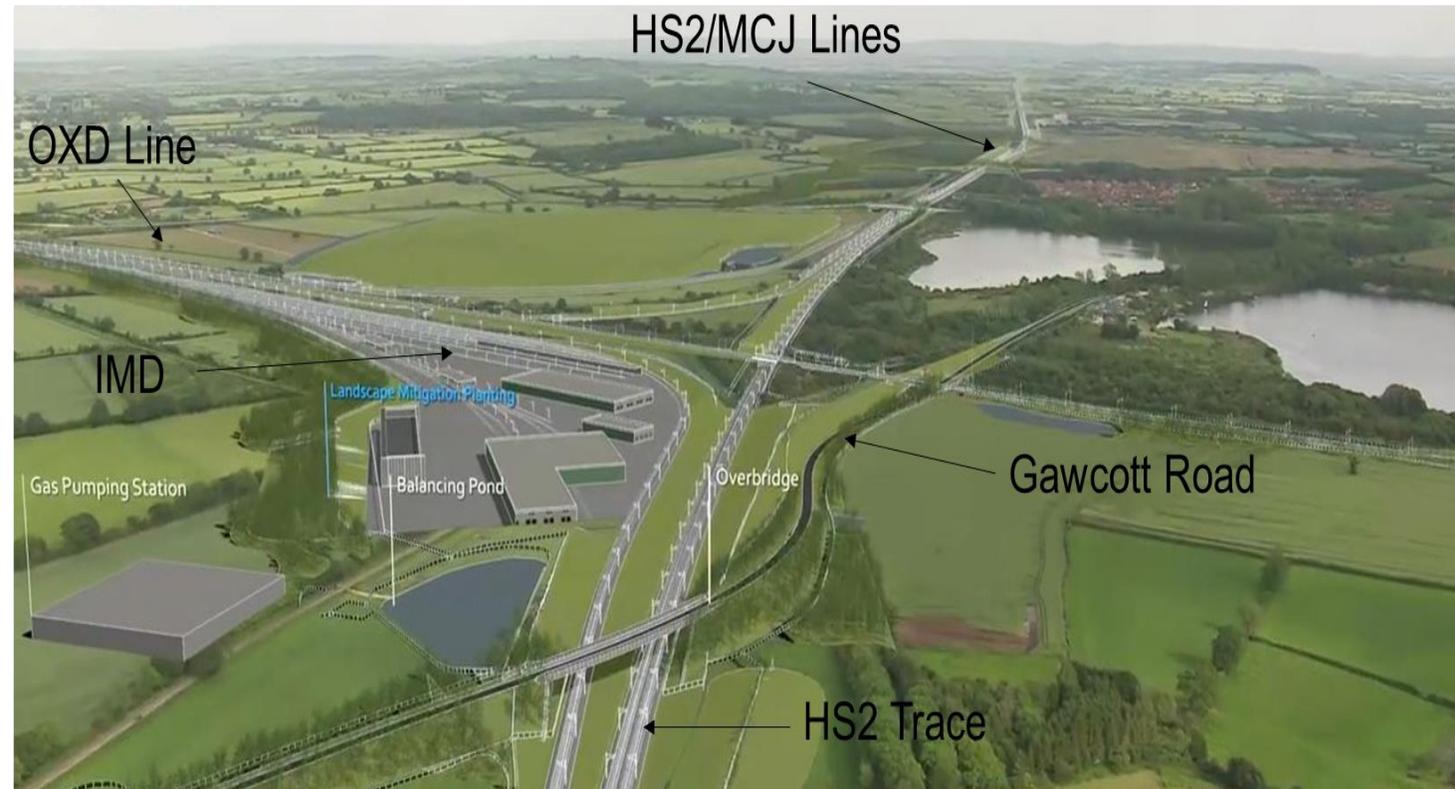

Progress Overview – Calvert North

SITE ACCESS ROADS

- School Hill At grade crossing – In progress (early Spring) 1
- SAR from School Hill – In progress

EAST WEST RAIL OB

- Pilecap West – In progress 2

CHARNDON LODGE UB

- Bases – In progress (early Spring) 3

PERRY HILL OB

- Piling works – In progress

ADDISON ROAD OB

- Top soil stripping & local ditches - **Complete** 4

SCHOOL HILL BATCHING PLANT COMPOUND




- Batching plant – Testing Priority Mixes – In progress

EARTHWORKS

- East - Removal of existing EWR embankment – In progress
- IMD Area – temp drainage – In progress
- Mass Haul roads - In progress
- CA Cutting South de-stumping – In progress (complete up to School Hill but on hold due to Fusion interface)
- CA Cutting North Temp pond – Complete

OTHER WORKS

- Shepherd's furze farm demolition works - Complete

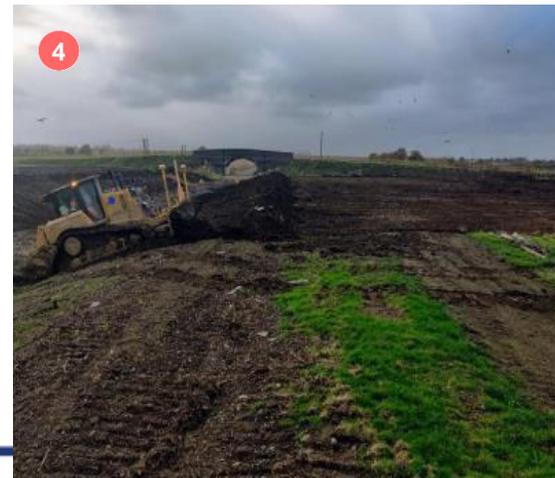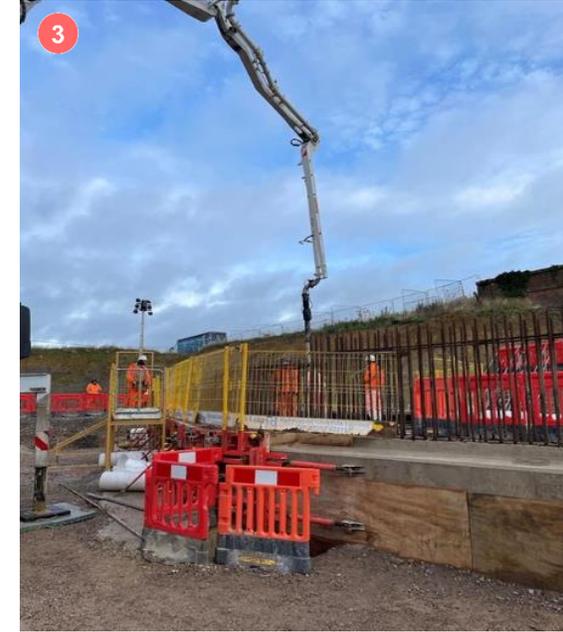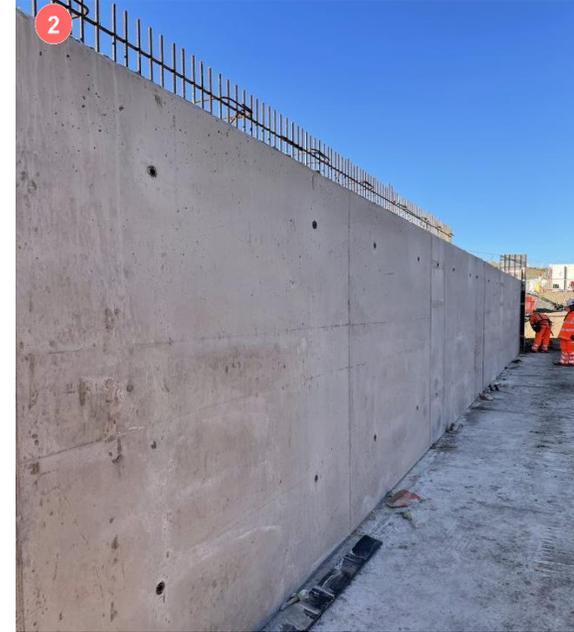

6 Week Lookahead – Calvert North

EWR OB 1

- Wingwalls bases
- West foundations waterproofing

Charndon Lodge 2

- East foundations waterproofing
- Backfilling
- Start abutment walls

Perry Hill OB 3

- Piling works (North abutment)
- Start excavation & piling cropping (South abutment)

Addison Road OB

- Excavation and filling

West Street OB 4

- Mobilisation for temp utility diversions

Earthworks

- Complete EWR removal embankment
- PROW diversions
- IMD Area – Temp drainage & culverts crossings
- CA Cutting – De-stumping

Site Access Roads

- School Hill crossing
- South of School Hill to FCC

Other misc. works

- Batching Plant – Operational



Aerial views 13/10/21

3 Month Lookahead – Calvert North

- Addison Road Bridge
- GUN28 overbridge
- Calvert cutting drainage ponds
- Drainage around IMD
- East-West Route Rail HS2 overbridge
- Charndon Lodge Underbridge - Foundations
- Perry Hill Overbridge – Foundations
- Detailed design



Complaints & Enquiries in December



Working partners

Description of Enquiry/Complaint Description	Complaint Sub Category	Date complaint Raised	Response time (working days)
Query about whether Calvert Jubilee Nature Reserve was still open to the public	Programme of works (Timeline)	01-Dec	2
Damage to vehicle from an ill placed road sign	Small Claims Scheme	06-Dec	2
Concern about water based works taking place and impact to live stock	Water Resources	10-Dec	In progress
Query regarding waiting times at temporary traffic lights	Programme of works (Timeline)	11-Dec	In progress
Utilities works cutting off access to property for residents	Programme delivery	07-Dec	1
HGVs driving through unauthorised route in Padbury.	Traffic and Transport	08-Dec	1
Tree felling on property boundary	Ecology	09-Dec	1

In December to date we received 3 complaints and 4 enquiries.


No common themes

We are responding in...

2

Working days

Calvert – Mending the Fence

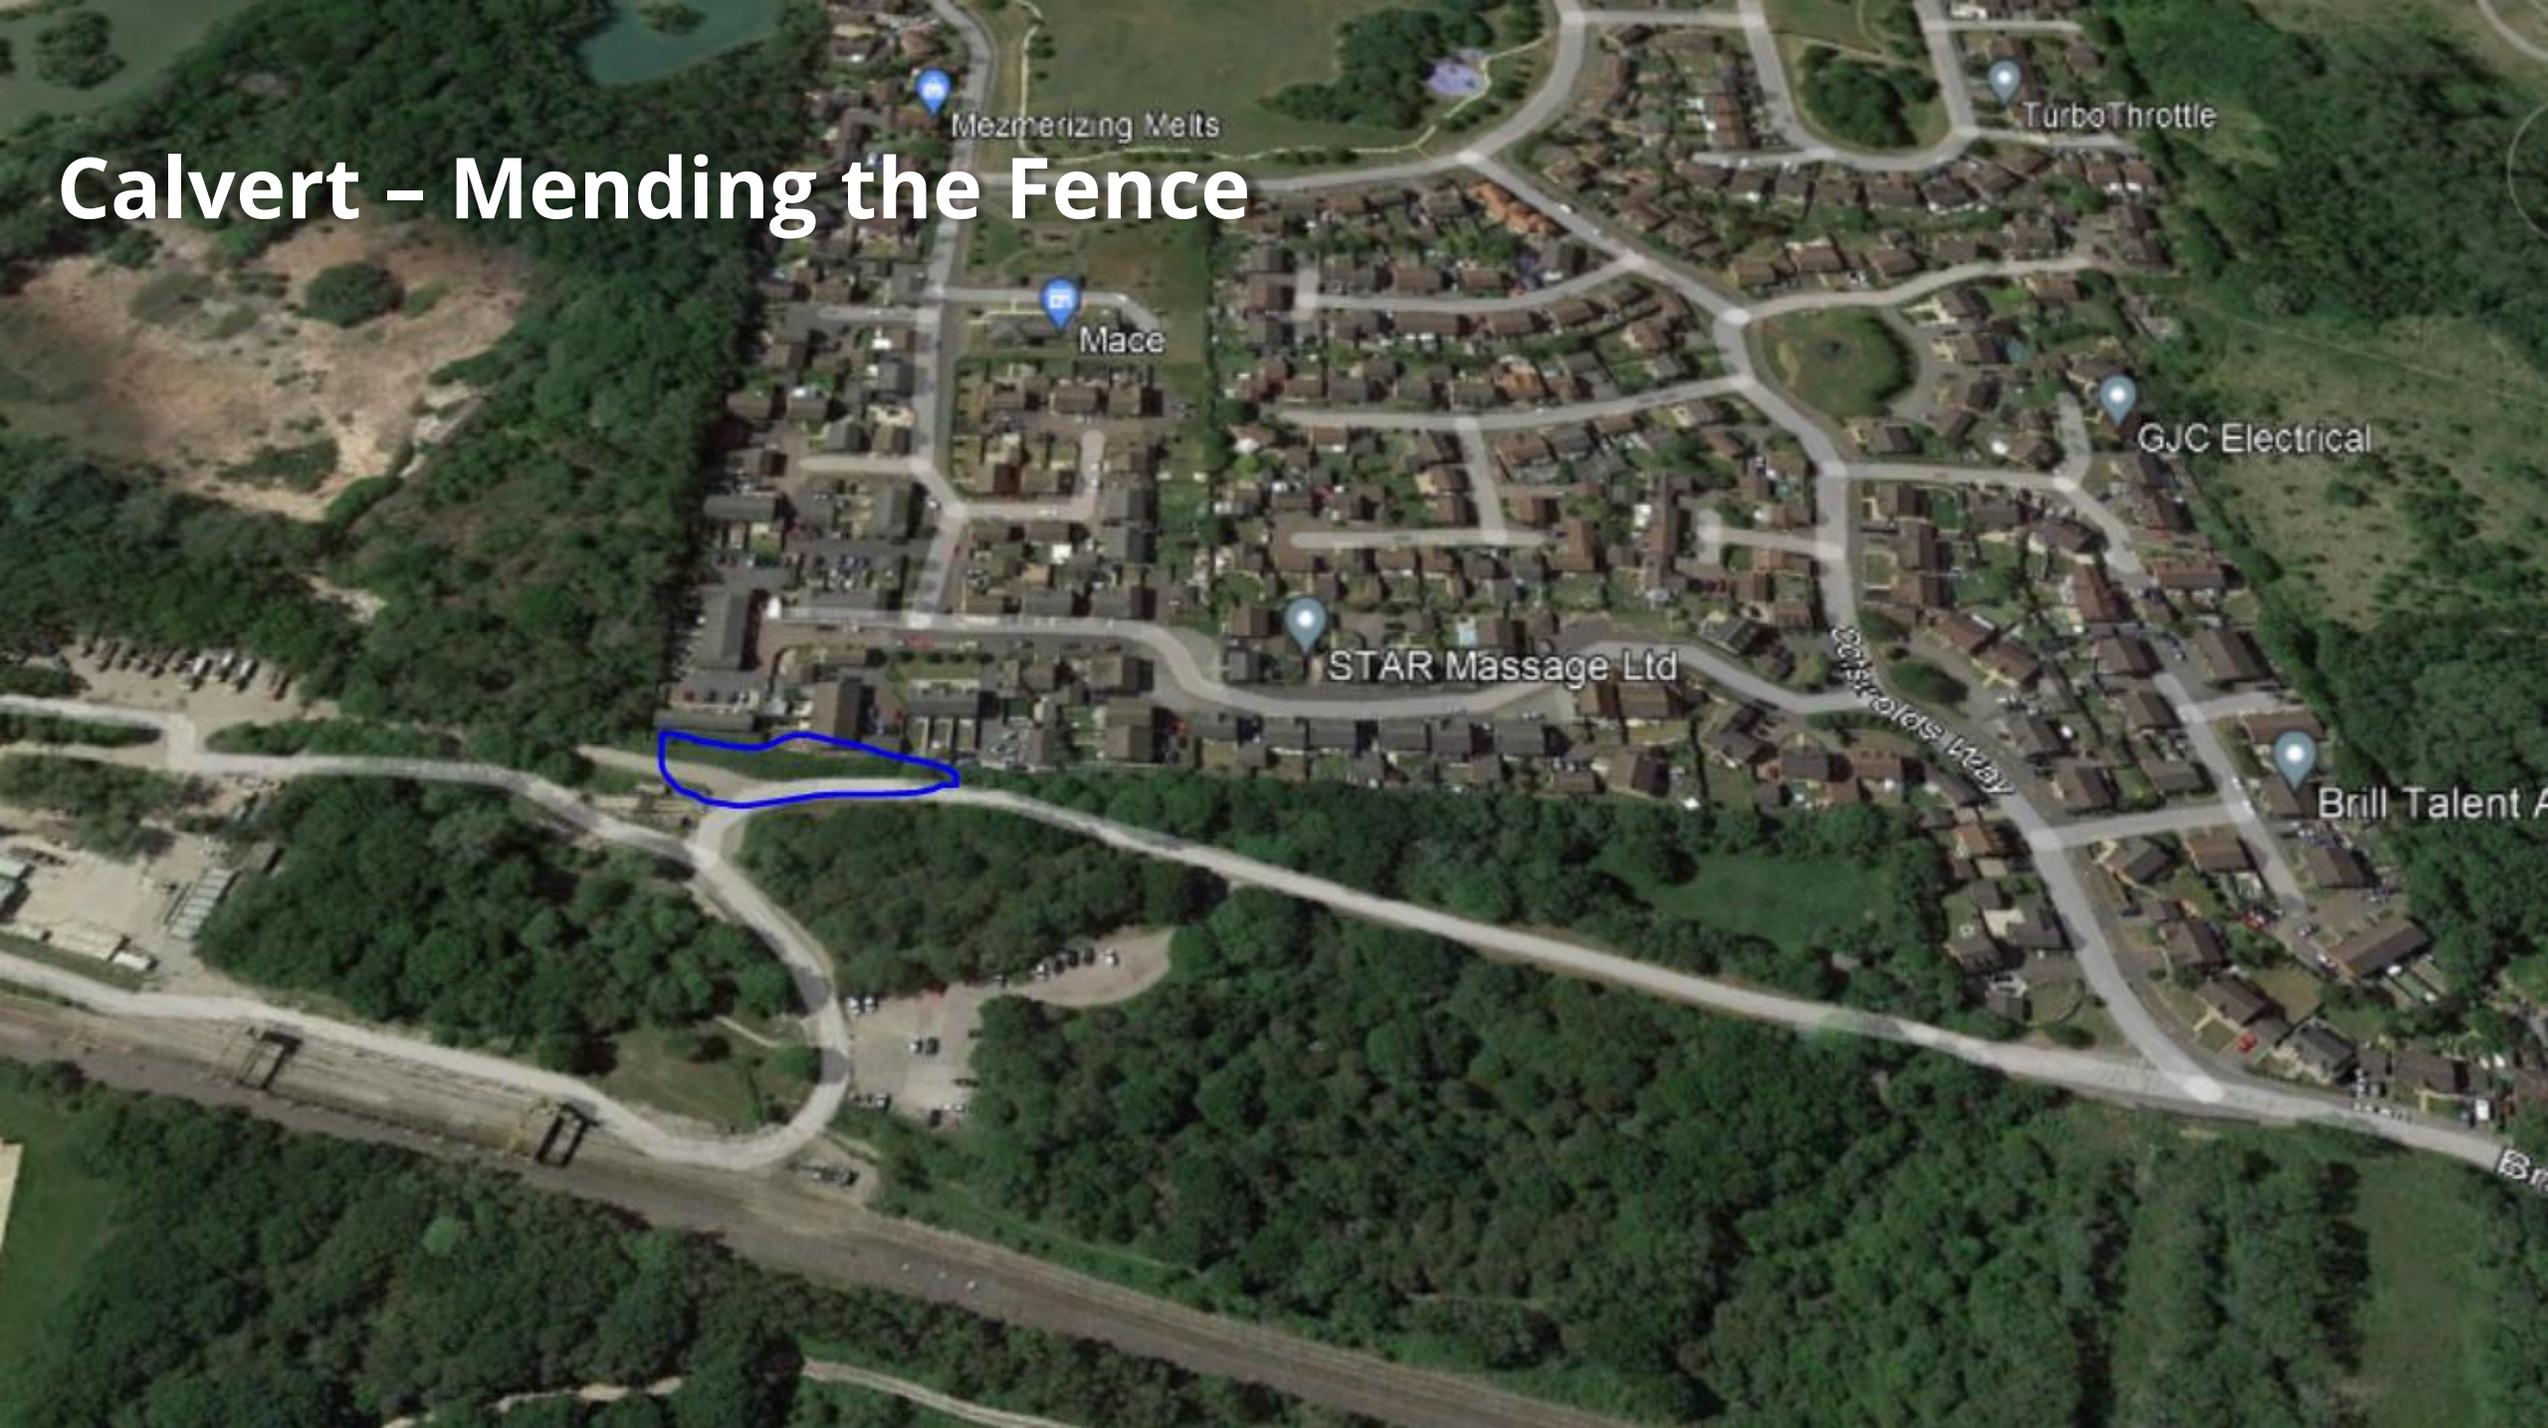


Calvert - Mending the Fence



Engagement Plan

- Newsletters
- Mobile Visitor Centre
- 3D models
- Face to Face limited until March..



General Update

Xmas Shutdown

- Shut down from Wednesday 22nd Dec. to Tuesday 4th Jan.
- Traffic management
- **Minimum lighting**
- Security cover
- HS2 Helpdesk
- **What Three Words**



Contact our HS2 Helpdesk team **HS2**

You can contact our HS2 Helpdesk team all day, every day of the year on:

Freephone **08081 434 434**
Minicom **08081 456 472**
Email **hs2enquiries@hs2.org.uk**

The graphic features a stylized tablet held by two hands. The screen displays the contact information. At the bottom of the screen are three circular icons: a green phone icon, an orange calendar icon, and a blue envelope icon.
